


EARTH BURGER HOUSTON

Fabrication, permitting coordination, engineering allowance, and installation for the complete Houston signage package.

EAST FRONT ELEVATION

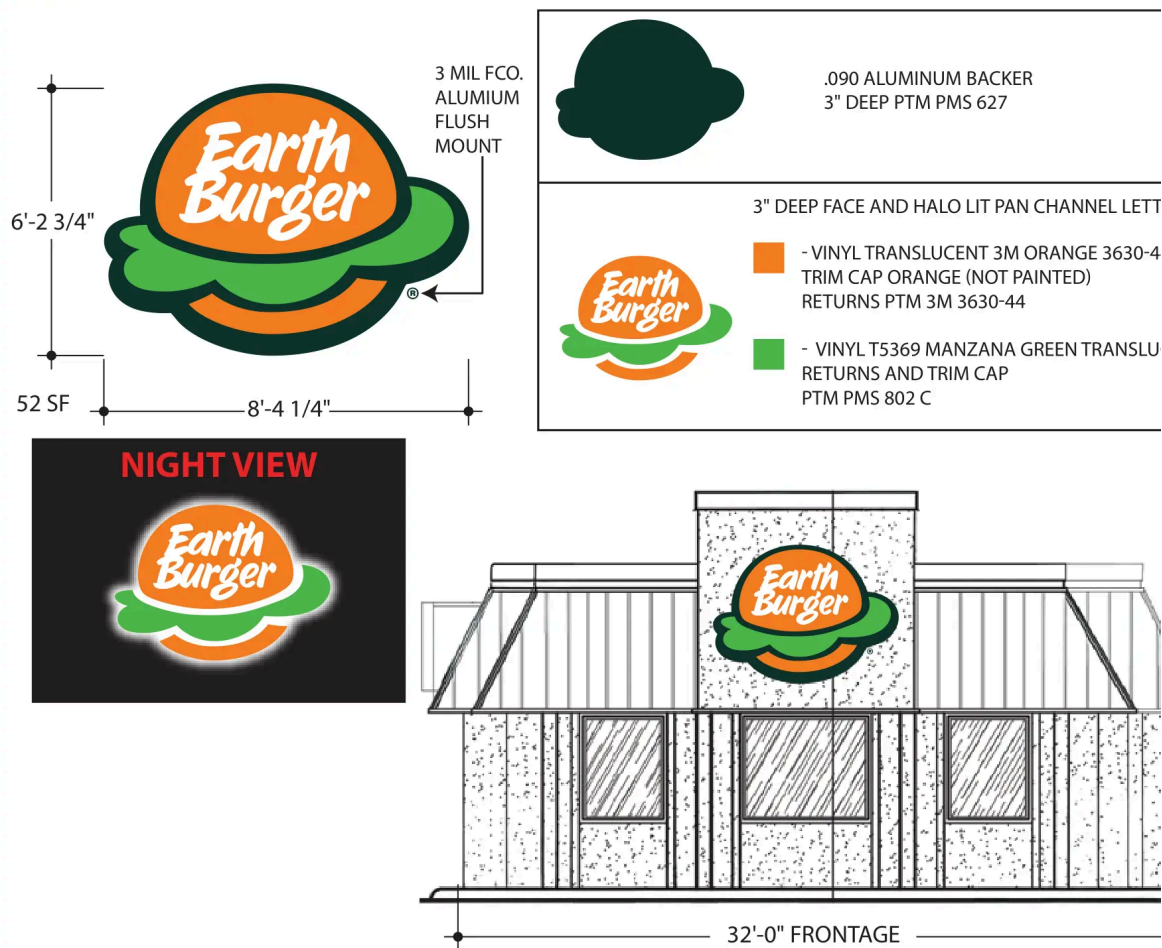

COMPLETE SIGNAGE PACKAGE

Project site	4640 Scott Street, Houston, TX 77004
Prepared for	Sinelli Concepts International

Proposal date

September 2, 2026

Valid through

September 17, 2026

Total project investment

\$47,250

before applicable sales tax

Scope basis: supplied ten-sheet signage package dated June 30, 2026.

Houston Sign Crafters proposes to coordinate, fabricate, permit, and install the complete signage package for Earth Burger #20001 at 4640 Scott Street in Houston. The scope is based on the ten-sheet signage drawing package dated June 30, 2026 and includes three illuminated exterior identity signs, drive-thru signage, wayfinding, a wall stencil, and three interior sign elements.

SCOPE + INVESTMENT

Every proposed sign and project allowance is shown below. Pricing is based on the complete package and the supplied drawings.

EXTERIOR IDENTITY \$19,300

+ East illuminated logo	\$5,100
+ South illuminated logo	\$4,600
+ North illuminated logo	\$8,900
+ South wall stencil	\$700

DRIVE-THRU AND WAYFINDING \$16,450

+ Drive-thru canopy structure (installation included)	\$13,350
+ Drive-thru wayfinding fixture	\$3,100

INTERIOR SIGNAGE \$4,050

+ Interior Veggie Joint letters	\$975
+ Interior round 100% sign	\$1,250
+ Entrance mixed-material sign	\$1,825

PROJECT DELIVERY AND ALLOWANCES \$7,450

+ Combined installation (all non-canopy signage)	\$5,000
+ Permit allowance	\$850

Total project investment

\$47,250

Applicable sales tax is not included

Deposit with agreement: **\$23,625**

Final payment upon installation: **\$23,625**

Package pricing may require revision if individual components are removed or materially changed.

"Houston Sign Crafters did an outstanding job from start to finish... The craftsmanship and attention to detail really stand out, and the whole process was smooth and hassle-free."

Francesco Tartamella · verified Google review of Houston Sign Crafters

HOW THE PROJECT MOVES

The sequence is built around Earth Burger's requested 90-day opening window. Agency review, approvals, and site readiness remain schedule dependencies.

1 AUTHORIZE

Execute the agreement and submit the 50% deposit.

2 VERIFY

Field survey and final dimensions, approximately 2-3 business days after site access.

3 ENGINEER AND PERMIT

Prepare required documents and submit after verified drawings. Review timing is controlled by third parties.

4 FABRICATE


Approximately 4-6 weeks after final artwork, engineering, and permit approvals.

5 INSTALL

Approximately 2-4 working days after fabrication, site readiness, and scheduling confirmation.

TARGET: REQUESTED OPENING WINDOW

DRIVE THRU CANOPY

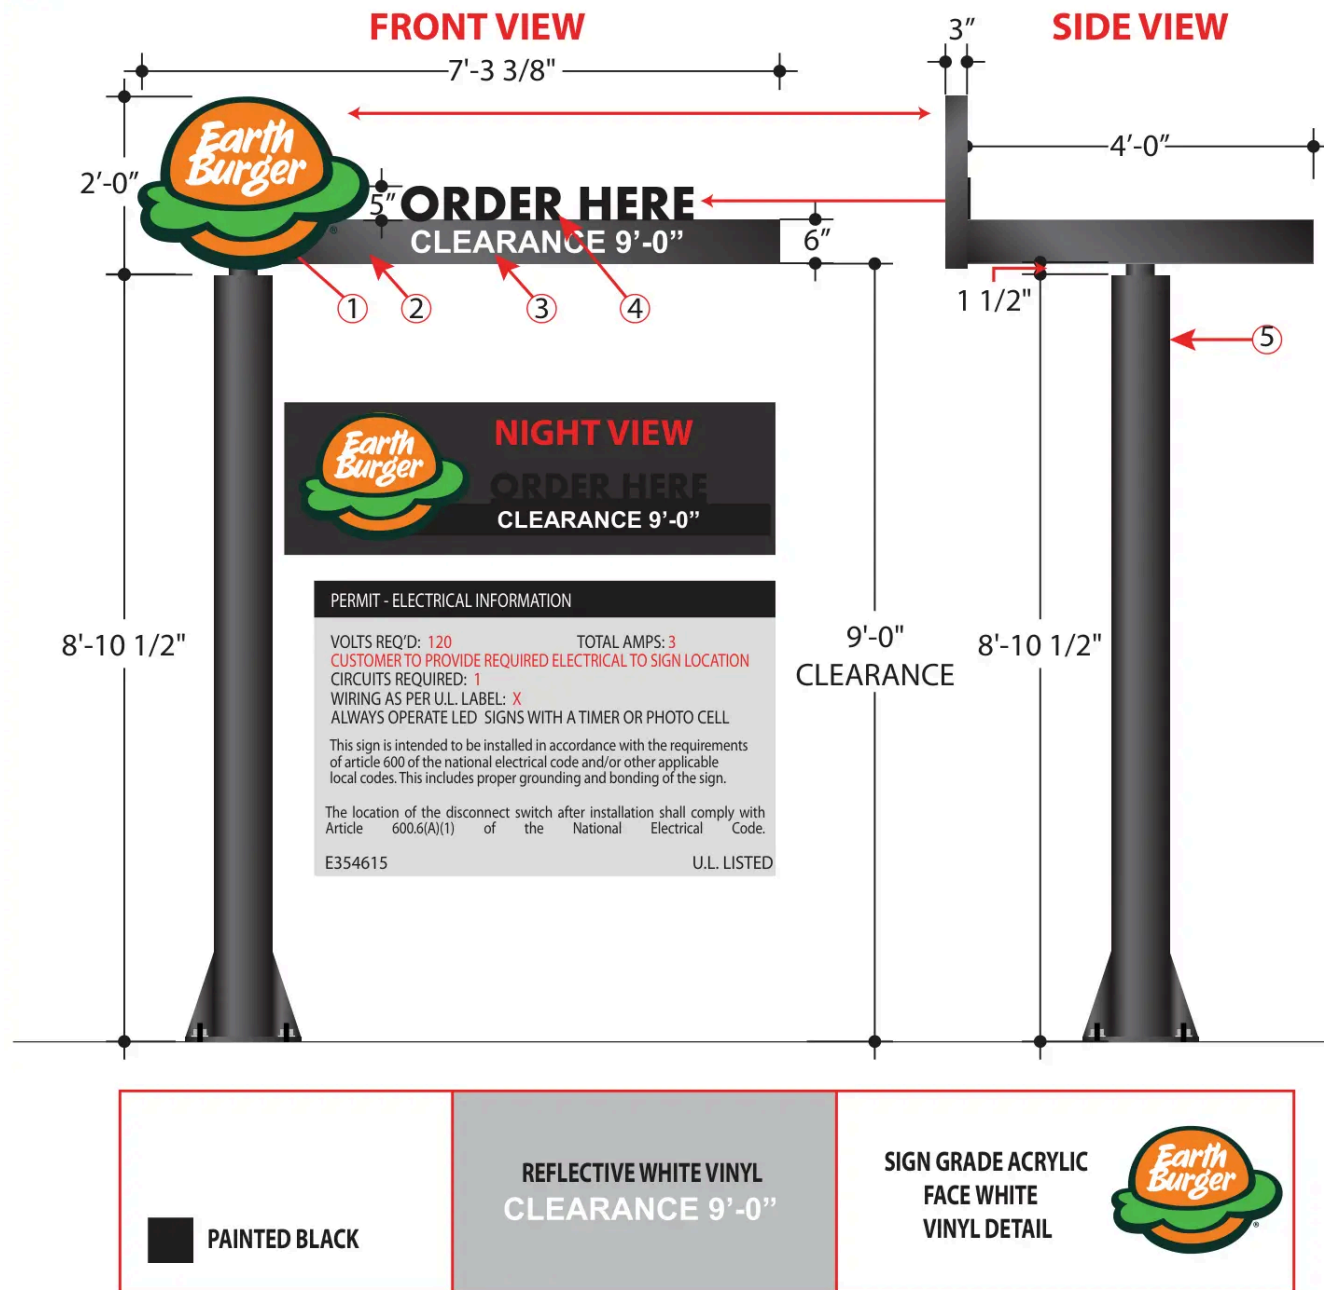

WHAT WE NEED FROM YOUR TEAM

- Final brand, artwork, landlord, and construction approvals
- Property and construction documents requested by permitting authorities
- Primary 120V circuits at each sign location
- Safe and unobstructed site access
- Drive-thru concrete base, anchor bolts, and J-hooks identified in the supplied drawing

- Final paint application for the south wall stencil

READY TO AUTHORIZE

The package gives Sinelli Concepts one Houston-based partner for field verification, fabrication, installation, and project closeout.



COMMERCIAL SUMMARY

Total	\$47,250 before applicable sales tax
Due with agreement	\$23,625
Due upon installation	\$23,625
Valid through	September 17, 2026

HOUSTON SIGN CRAFTERS INCLUDES

- ✓ Field verification and project coordination
- ✓ Listed fabrication and installation scope
- ✓ Standard permit and engineering coordination
- ✓ Installation scheduling and closeout
- ✓ Five-year limited warranty on qualifying HSC-fabricated electrical signage

ELEVATION AT ENTRANCE AREA INTERIOR SIGN

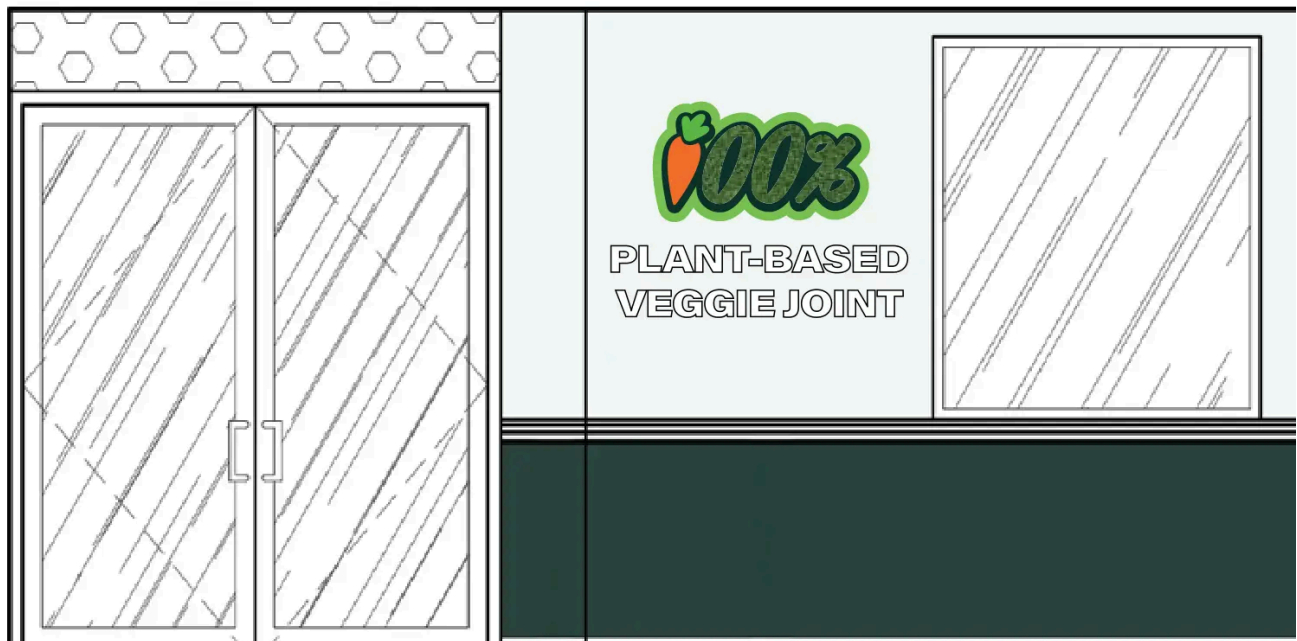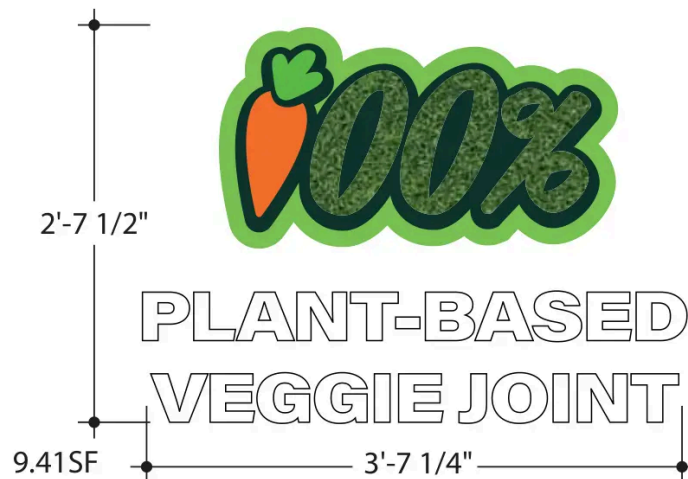

IMPORTANT CONDITIONS

1. Permit or engineering costs above the stated allowances require written approval.
2. Final dimensions and attachment methods remain subject to field verification.
3. Concealed conditions, inadequate structure, unavailable electrical service, underground conflicts, scope changes, remobilization, storage, and after-hours work are excluded unless authorized.
4. Changes may affect both price and schedule.
5. The final fabrication and installation agreement controls if it conflicts with the proposal page.

WHO RUNS YOUR PROJECT

Rameel Sheikh

Owner, Houston Sign Crafters

Direct: (832) 974-2546 · sales@houstonsigncrafters.com

NEXT STEP

REQUEST THE AGREEMENT

Then we will schedule the field survey and confirm the permitting and production path.

sales@houstonsigncrafters.com · [\(832\) 974-2546](tel:(832)974-2546) · 1359 E 40th St, Houston, TX ·
[Download PDF](#)

Prepared and submitted by

Rameel Sheikh

Owner, Houston Sign Crafters · September 2, 2026

Houston Sign Crafters

1359 E 40th St, Houston, TX

(832) 974-2546 · sales@houstonsigncrafters.com · Proposal #HSC-EB-20001

Confidential commercial proposal prepared for Sinelli Concepts International.

